NUBANK // BUSINESS CASE

Chief of Staff to the CFO & Global Corporate Governance

Cassio Modelli - October 2026

1 | IN-HOUSING PLANNING & BUDGET TRADE-OFFS

$60M of asks vs. a $25M cap

Centralizing planning to improve alignment and coordination, while driving investment/expense discipline and methodology

2 | C-SUITE ALIGNMENT & BOARD GOVERNANCE

Board meeting cadence and prep

Establishing agenda rhythm and material preparation efficiency + ways of working to navigate executive priorities and support alignment

3 | SPECIAL PROJECT NEGOTIATION

A new HQ: complex workstreams

Leading cross-functional engagement without hierarchy to incorporate specialist input and lead to better outcomes

THE FOUNDATION: FINANCE & GOVERNANCE AS GROWTH LEVERS AND BUSINESS ENABLERS, SUPPORTING NUBANK'S GROWTH AMBITIONS BY ESTABLISHING WAYS OF WORKING TO REMAIN AGILE WHILE ADDING RIGOR REQUIRED BY SCALE.

PROPOSED APPROACH

Establishing principle-based structure for each deliverable

OWNERSHIP as a core principle guiding all four topics: Proposing methodology, gathering data/viewpoints, providing recommendations and options, establishing decision management criteria. Decisions, rationale and dissent are recorded for processes and outcome continuous improvement

DELIVERABLE 1 // PLANNING

Global Planning Hub + spend discipline

CoS & CG and Global Finance / FP&A stand up a Planning CoE with the Countries and GMs: one Nubank

Business case methodology for spend prioritization + proposed funding schedule.

DELIVERABLE 2 // BOARD

Establishing cadence and ownership

Agenda topics are living concepts – updates are key.

The book ships 7 days before the Board, every quarter.

Decision framework: positions, voting & CEO arbitrage

DELIVERABLE 3 // HQ

120-day gated approach

What can we do?

What may we offer?

Who may bind Nu?

Do we commit?

Our team recommends; the CEO and CFO decide.

DELIVERABLE 4 // LEADERSHIP

Built with, not for

This team will work inside the business and its numbers: we propose, implement, assess, and change course fast.

AI-enabled processes to support integration.

The CFO owns the decision.

How will we measure success?

The CoS & Governance team acts as equal parts catalyst, facilitator and trusted advisor to drive (1) 100% of discretionary spend released against an approved case, with cycle time under 40 days; (2) a living Board agenda, with the book out 7 days before every Board; (3) HQ gates 1 and 2 cleared by mid-December, nothing signed between gates; (4) the team rated twice a year by the GMs as a growth facilitator, not corporate bureaucracy. Decisions requested today: the $25M FY27 cap and its release schedule, the Board calendar, and the HQ gates.

A lean hub and three meetings to centralize planning

THE CENTRALIZED PLANNING STRUCTURE

A CoE hub of 4-6 people

CoS & CG partners with Global Finance / FP&A to stand up the CoE; the hub and market/vertical teams report to Global Finance, with a dotted line to Country CFOs.

KPIs: cycle time under 40 days, forecast accuracy, and 100% of discretionary spend with an approved case.

AI-enabled processes: agents to support consolidation, tracking action items, facilitating alignment and reducing manual work.

Career pathways: “seeding” talent across markets.

Meeting	Who runs it	Output
Stand-ups, bi-weekly	Global Planning + Local Finance	Data gathering, alignment on drivers, reporting best practices
CFO 1:1s, monthly	CoS & CG team + Country CFOs	No surprises at the lock and asks knowing path to approval
GM Reviews, quarterly	Global CFO & CoS + GMs/Business Leaders	Tracking of strategic projects, prioritizing spend and investments

Ways of Working: Local Finance teams own the FP&A drivers and business case assumptions; CoS & CG team standardizes, consolidates and provide analysis and insights; the CFO makes decisions on spend and reports results to the board. Global Planning becomes a key resource to inform Senior Management on what we are doing, what’s working or not, and how those inputs inform decision-making.

RISK

Without Country buy-in, model can drive Local vs. Global inaccuracy/misalignment

In-market presence and alignment with local CFO/GM agendas are crucial.

RISK

Mismatched job descriptions and leveling to existing structures

Roles and responsibilities clearly established and assimilated to inform who does what

RISK

Governance can be perceived as bureaucracy and loss of speed

Leveraging AI processes to speed up manual work helps avoid the pitfalls seen in large companies

DELIVERABLE 1 // TEAM

Hub of 4-6: 2-3 in the countries, 2-3 central in the US, in two waves

Role	Level (proposal)	Where	Reports to	Wave
Hub lead: CoS & Corporate Governance	Existing role	US (central)	Global CFO	In place
Global planning manager: owns the model, the case template and the release packs	Senior manager	US (central)	Hub lead	1: by Q2'27
Finance partner, Brazil: cases and drivers with the GMs and the Brazil CFO	Manager / senior manager	Brazil	Global Finance; dotted line to the Country CFO	1: by Q2'27
Finance partner, Mexico: same role for Mexico (and Colombia until wave 2)	Manager	Mexico	Global Finance; dotted line to the Country CFO	1: by Q2'27
Decision-support analyst: data platform, AI agents, consolidation	Senior analyst	US (central)	Global planning manager	2: by Q4'27, if gates pass
Finance partner, Colombia	Manager	Colombia	Global Finance; dotted line to the Country CFO	2: by Q4'27, if gates pass
Second central analyst (only if volume requires)	Analyst	US (central)	Global planning manager	2: by Q4'27, if gates pass

Quality gates for wave 2 (checked at the H1 close): wave 1 in seat and onboarded; cycle time under 40 days on the Q1'27 release; 100% of first-release spend with an approved case; forecast-accuracy baseline set in Q1 and improving in Q2; mid-year GM feedback positive. If a gate fails, wave 2 waits and the gap is fixed first.

Proposal. CoS & CG partners with Global Finance / FP&A to stand up the CoE; the central roles sit with Global Finance in the US. Levels map to Nu's leveling at hire. Country partners are market hires, not relocations. Hiring cost is central opex and counts against the $25M cap. Wave 1 recruiting starts after the Board; wave 2 only on the gates above.

Prioritized staged deployment > flat cuts across the board; the precedent and the discipline matter more than the nominal asks

THE GAP ($60M of asks vs. a $25M cap):

$35M

Equal to:

~15 bps of annualized revenue

~1.1% of annual opex

~0.2 points of efficiency ratio

Drivers: Efficiency ratio 19.5% in Q2'26 (17.6% in Q1); FY26 expected near 20%. Cost to serve $1.0 a month ($0.8 a year earlier) against $17.1 of ARPAC.

Problem statement: Asks as numbers with no pre-defined, globally standardized format for valuation and assessment. Establishing the approach is a tone-setter; proper discipline and decision-making support will inform how we prepare for investment and expenditure as we scale.

Three ways to close the gap	Why
Equal cut (every unit gets 42% of its ask)	Fast, but it shows a path to pad next year's ask
Core markets first (pause new bets)	Simple, but new bets lack focus/funding
Business-case readiness and staged release (recommended)	Wins on growth return, ownership, value creation; trade-off on speed

Budgets can work like Nu's credit management principles.

Nu's 20-F Form describes "low-and-grow": small limits, raised on behavior.

Budgets should get same test-and-learn: start small, grow when KPIs (i.e. activation, 30-day retention, unit cost) can support further scaling. This becomes an ownership-driving, principle-based methodology.

Sources: Nu Q2'26 release and 6-K (opex $806.2M; net revenue ~$4.1B a quarter), Q2'26 call, Form 20-F. Calculations: the 15 bps is on managerial revenue, ~$23.5B annualized; the 1.1% is on opex, ~$3.2B annualized; the efficiency-ratio points are on Nu's denominator (NII plus fees).

DELIVERABLE 1 // PRIORITIZATION

Proposed investment and spend prioritization framework

Mandatory obligations pass a separate gate, and discretionary asks compete within agreed strategic envelopes.

PROPOSED SCORECARD // DISCRETIONARY ASKS

Criterion	Weight	Evidence required
Strategic contribution	**25%**	Priority + measurable outcome
Economic value	**30%**	NPV, payback + downside case
Customer / risk impact	**20%**	Customer KPI or risk reduction
Delivery confidence	**15%**	Owner, capacity + dependencies
Speed to evidence	**10%**	Time and cost to validate

Rate 1–5 against published anchors.
Score / 100 = Σ(weight × rating / 5).
Finance tests downside assumptions and ranking sensitivity.

DECISION PROCESS // CLEAR OWNERSHIP

1 Intake and hard gates

Business + Local Finance submit one case: full cost, baseline, alternatives and benefit owner. Legal / Risk validate mandatory scope when applicable.

2 Challenge and rank

Global Planning calibrates scores across markets. Compare core and new bets within agreed envelopes using horizon-appropriate KPIs.

3 Decide and release

CFO approves within delegation and the cap. CEO resolves strategic trade-offs. CoS & CG records rationale, dissent and next-gate KPIs.


4 Track and reallocate

Owners report actual spend and benefits monthly. Global Planning consolidates and reviews quarterly with CFO, which decides further releases / deployments.

Proposal: weights and cadence require CFO agreement. Method draws on McKinsey capital-allocation guidance (2023, 2024).

DELIVERABLE 1 // SCHEDULING

Proposed path: fund now + stage, assess, go/no-go

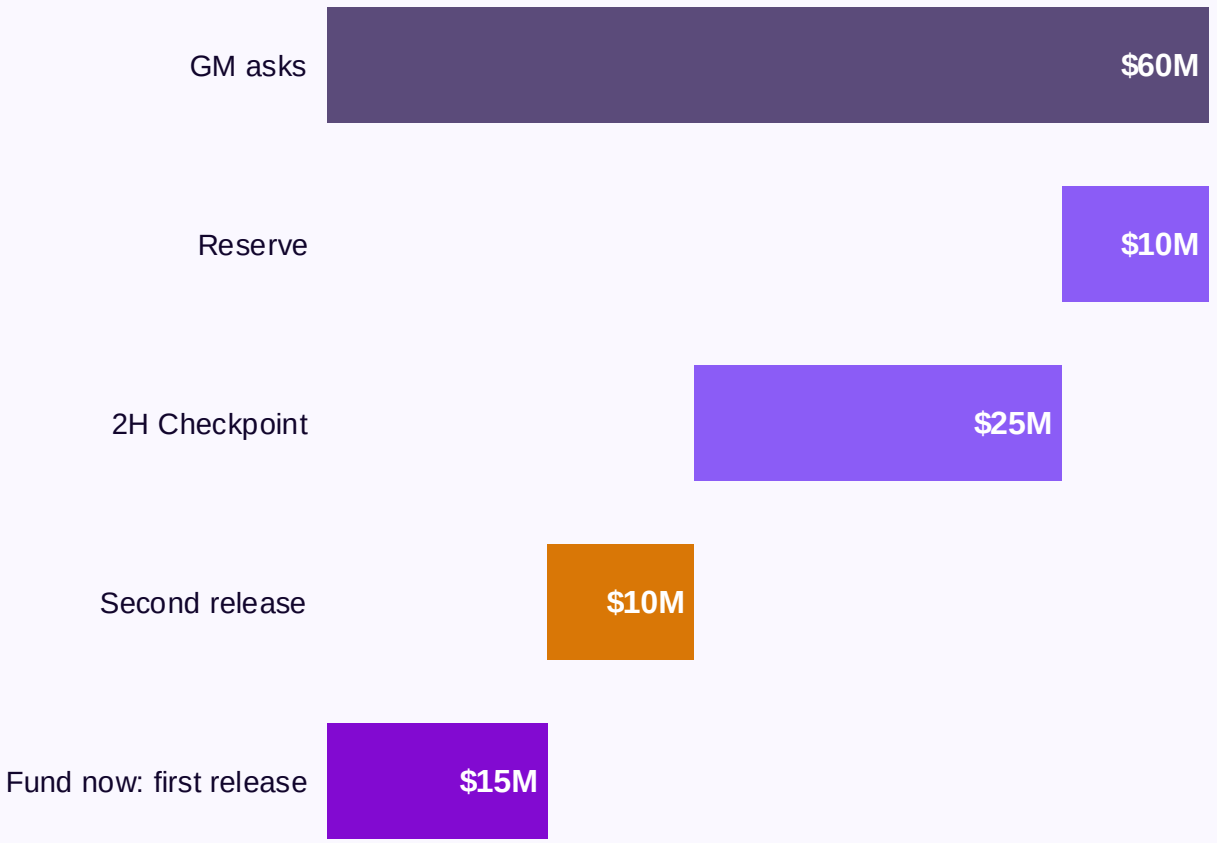

FUND NOW // FIRST RELEASE 1Q27, SECOND RELEASE 2Q27

$15M - $10.5M to core markets (70%) and $4.5M to new bets (30%), for cases vetted through the proposed methodology.

$10M - Second release to asks for Business where Q1 results support additional investment, decided on Q1 data.

STAGE-GATE // LATE FISCAL YEAR RELEASE, 3Q-4Q27

$25M - Released to Business units on track to beat the FY27 plan, decided at the H1 close on H1 data: only from profit above plan, inside the efficiency-ratio guide in force, with NPL 90+ on plan (the CFO decides; Risk can block). Remedial spend for units behind plan goes to the MTeam, with CFO prioritization.

DEFER // Q4 RESERVE

$10M - Set aside for strategic imperatives, special projects, regulatory requirements or similar extraordinary escalation factors, and deployed after MTeam validation.

The two releases ($25M) are the cap. The 2H checkpoint (up to $25M) and the reserve ($10M) sit outside the plan and open only on the conditions stated, so every dollar of the $60M has a path. The 70/30 split follows mature cohorts: ~$31 of monthly ARPAC at eight years against $17.1 for the group (Q1'26 cohort data).

CoS & CG: Ways of Working

The CoS & CG lead drives alignment and resolves executive differences; the team registers Board decisions, tracks progress and consolidates data and insights from Business Units.

ACCOUNTABILITY

CoS & CG lead

Fosters alignment with executives before formal decisions. Takes unresolved trade-offs to the CFO, always with a recommendation.

Core team

Runs the calendar. Prepares briefs and tracks actions. Leverages AI Agents for efficiency. Liaises with Country/BU teams.

Decision rights

Executives own the content. The Chair approves the agenda. The Secretary manages formal governance and minutes. The CoS & CG team reports.

WORKING CADENCE

When	Who	Purpose / deliverable
Weekly	CoS & CG lead + CFO	Alignment on strategic topics, Finance management agenda, MTeam / Board priorities
Monthly	CoS & CG lead + CFO + GMs	Discuss topics, pending points and decisions needed for the next two Board meetings.
Before Board	CoS & CG team + Finance teams	See proposed prep schedule: T−28 scope, T−16 resolve differences, T−10 final inputs, T−7 publish.
After Board	CoS & CG lead + CFO	Within 5 working days, confirm actions and dates, and provide progress reports on strategic items.

Each meeting has an executive sponsor, an agenda, a meeting cadence and decision tracking.
Action items have an owner and due date. The team flags delays weekly; material issues get escalated to the CFO.

Proposed operating model. Advisory basis: McKinsey (2023) and DirectorPrep (2024). T = Board meeting date.

Board Prep Target: Every quarter the book goes out 7d before the Board

Hypotheses on why the book is late: no central ownership, no locked outline, no standard formats and templates, and units building misaligned decks.

T-28 TO T-21

Outline locked

We issue the locked outline and standard data tables, so units stop building rival decks.

T-20 TO T-14

Executive lock

One-to-ones at T-21. The options memo settles the capital priorities and the 70/30 core / new-bets split with the CEO and CFO at T-16.

T-13 TO T-7

One pen

Inputs freeze at T-10. Committee chairs are briefed at T-9. The book is on the portal at T-7.

T-6 TO T-0

Decisions, not read-outs

Directors' questions are answered in writing by T-3, so the meeting goes to the capital plan.

Two items cannot slip: the capital plan, because this is the last Board before Investor Day on 8 Dec, and the statutory items for new entities: open an entity only when a license or tax substance requires it; officers and signing follow the stage (backup B).

RISK

Still no agreement at the lock

Dissenting positions go in the memo; the CEO decides; the dissent is recorded, so the Board sees one recommendation.

RISK

Materials are still late at T-10

The locked outline decides: anything outside it goes to the appendix or the next meeting.

RISK

The book holds non-public Q3 results

Portal only; IR sets what directors may discuss. The review agent's drafts run on Nu-approved tools, and a named owner signs each answer.

Board assumed on Tue 17 Nov, four weeks from today. Q3'26 results are due 12 Nov; Investor Day is 8 Dec 2026.

Managing different viewpoints and friction at the executive level

STEP 1

Talk privately first, always

C-level access comes with earning trust and a seat at the table. Understanding the GMs' priorities is key to drive acceptance as an advisor; the Business must see this role as an enabler and advisor, not a blocker.

STEP 2

Move beyond facts and numbers

From "I need $25M" to "what would prove this justifies the ask?" - the governance sets the bar, and this team gains buy-in working as a facilitator to navigate the requirements for a path to approval.

STEP 3

People, people, people

Establishing access with teams, not just leaders, is a proven path to (a) acquire "finger on the pulse" insights, and (b) show executives that this is a generalist team that can navigate a multitude of topics engaging the SMEs

STEP 4

Build with, not for

Making GMs and teams feel part of the solution is a virtuous cycle to secure alignment and increase synergy - REAL synergy that comes from a well functioning, high-performance executive team focused on shared goals.

Why it can work without line authority: the CoS & CG can play a crucial role in selling the value of the governance and why it makes our decision-making process better. GMs don't need to agree on everything all the time, but the rules are public on day one, the tough conversations are private, and the sign-off is joint even upon disagreement – "dissent but commit" is a solid outcome.

Fair process: Kim and Mauborgne, "Fair Process: Managing in the Knowledge Economy", Harvard Business Review.

The HQ is a governance project as much as a real-estate deal

THE ASSESSMENT

What needs to be assessed before a site is defined and a lease / purchase can happen

A regional hub and campus, negotiated across Legal, Tax, Compliance, People and Workplace, exists in more than one jurisdiction with no clear owner over all of them. This is an enterprise initiative that requires significant cross-functional work, with proper cadence and discipline to run it.

WHAT IS NEGOTIATED

Different kinds of agreements

Local regulatory agreements: the incentive or grant, any tax ruling, registrations and permits, work permits (Legal, Tax, Compliance, People, Government Engagement).

Campus infrastructure agreements: lease or build-to-suit, fit-out, utilities, land and zoning (Workplace, Legal, Tax).

PRINCIPLES ON CHOOSING A SITE

Four hard tests, then five criteria

1. **Regulatory**: Nu has the required licenses for what the hub's activities require (Compliance, Legal).

2. **Tax**: people and decisions there do not move Nu Holdings' tax residence or create a taxable presence (Tax, Finance).

3. **Officers**: Nu can field directors who pass fit-and-proper requirements (Legal, People).

4. **Substance**: real payroll and assets, so the incentive survives Pillar Two (Tax, People).

Then five weighted criteria: talent and wage cost; incentive net of clawback; campus cost and timing; modeled tax rate; political and reputational risk (suggested weights in backup J).

Propose to start where Nu already has licensed substance and a local CFO (Brazil, Mexico, Colombia) or is building (the US). Two sites go to term sheet, then the CEO and CFO prioritize

Nu Holdings is Cayman-incorporated (Form 20-F). Nu is above the EUR 750M Pillar Two threshold; 15% minimum; the 2026 carve-out is 9.4% of payroll and 7.4% of tangible assets (OECD GloBE, Art. 5.3 and 9.2). Brazil applies a domestic minimum top-up tax from 2025. Jurisdiction open; no savings figure until a site is chosen.

SMEs own the judgment, CoS & CG owns the process, the CFO owns ultimate recommendations

STATUTORY OFFICERS

Authority and safeguards

Gate decisions are taken at the monthly SteerCo, chaired by the CFO.

Signing: central until gate 3, then delegated limits.

Officers: qualified appointees, with D&O cover before activation.

Legal confirms personal liability. Regulatory filings start at gate 1.

Regulated entities need a capital plan and Board oversight.

CROSS-FUNCTIONAL LEADERSHIP

Accountability and escalation

CoS & CG leads cadence and delivery; functions own the technical advice.

CFO recommends, CEO selects the site; board appoints officers.

Weekly functional leads meeting with one decision log; monthly SteerCo.

When functions disagree, both views go in the log and reach the CFO within 48 hours with a recommendation; Legal and Compliance keep legality vetoes.

RISK

Tax residence planning changes

Opinion at gate 1; meeting patterns unchanged; no early signing (Tax).

RISK

Officer approval runs late

Files at gate 1; no activation before approval; the lease long-stop moves with it (Legal, People).

RISK

Dependence on the CoS

A named deputy is the de facto #2 in command of the project; the data, documents and decision log exist in cloud shared environments

Signing limits and the delegation model are proposals. If the hub sits inside an existing licensed entity, gate 3 shrinks to a powers-of-attorney update (backup B). Full HQ risk register and site scorecard: backup J.

Proposal: Four decision gates in 120 days; nothing signed between them

Gate	Owner	What we negotiate	Exit test	Walk-away
Gate 1, D+30: can we? Tax and residence	Tax, with Compliance	Nothing yet: internal	Tax-residence and taxable-presence opinion for both sites; modeled tax rate holds under Pillar Two; Compliance confirms permission	Any site where residence or a taxable presence moves, whatever the incentive
Gate 2, D+60: what may we offer? Regulatory and grant terms	Legal, with Tax	Incentive agreement with prospects; commitments only inside the published plan	Signed term sheet: negotiate 12-24 months' grace; one site dropped by elimination criteria	A cliff-edge clawback; a headcount commitment above plan; terms that bind other markets
Gate 3, D+90: who may bind Nu? Officers and signing	Legal and People	Nothing external: Nu's own governance	Officers named from licensed executives; fit-and-proper files in (started at gate 1); signing matrix and powers of attorney approved	Any appointment without Compliance/Legal cover or regulator approval
Gate 4, D+120: do we commit? Lease and campus	Workplace, with Legal	Lease or build-to-suit, fit-out, utilities, infrastructure contribution	Lease inside the FY27 plan, cost phased, a break option matched to the grant's grace, a long-stop date tied to gate 2	No break option, or cost committed before the incentive is signed

CoS & CG acts as the PMO / project lead to gather inputs from involved stakeholders, establish progress tracking, provide assessments and recommendations, and support MTeam decision-making discussions.

Leadership approach: trust, accountability and follow-through

TRUST

Business partnership

Understand GM priorities through private conversations. Work with Country and BU teams, engage their experts and develop recommendations together.

ALIGNMENT

Clear recommendations

Make criteria explicit before decisions. Resolve differences privately. Bring unresolved trade-offs to the CFO with a recommendation and a record of dissent.

EXECUTION

Visible accountability

The lead aligns executives. The team runs the calendar, prepares briefs and tracks actions. Every commitment has an owner and date. AI supports analysis, people validate it.

LEARNING

Regular course correction

Start with a clear proposal and review date. Use quarterly reviews to assess results and change what is not working. Seek GM feedback twice a year.

Working discipline: weekly CFO alignment, monthly GM discussions and Board preparation against agreed deadlines.
Track actions after each Board. Escalate material issues promptly. Keep local decision rights and specialist governance intact.

Proposed approach. Fair process: Kim and Mauborgne (HBR).

Working with the markets: who owns what, and how we learn

Topic	CoS & CG owns	CoS & CG influences	GMs and Local/BU CFOs own
Planning	One working model; alignment with Geographies and Functions; the investment business case requirements and template; a read of every first-release case before the lock	GM/CFO one-to-ones; the Board prep with the CEO and CFO; IR and Investor day prep	The P&L numbers and drivers; rationale and data behind asks; local CFO-level decision rights
Board	The board prep timeline and schedule; the coordination with stakeholders; tracking topics and projects; reporting results and outcomes	MTeam alignment; prioritization; business case for capital asks	The narrative and positioning; supporting the Board/IR calendar with data; adhering to the timeline and schedule
HQ Project	The SteerCo cadence and materials; consolidation and driving the agenda with SMEs; the decision log and the site scorecard prioritization	Discussions and insights for executive assessment; CFO/CEO decision-making support	Technical judgment (Legal, Tax, Compliance); signing (licensed executives)

Propose, implement, assess. Each quarter CoS & CG and the CFO review what's working and what can be improved: keep, fix or drop. The function earns its place with the markets instead of ruling from HQ and contributes to better alignment and discipline without compromising speed.

Backup

A Key assumptions | B Statutory entity model | D Sources
F Day-by-day timeline | H AI support | J HQ site scorecard and risk register | K How AI was used

BACKUP A

Key assumptions and the facts they are based on

Statement	Class	Basis
Nu Q2'26: 138.9M customers, monthly ARPAC $17.1, cost to serve $1.0, efficiency ratio 19.5%, ROE 33%, net income $1.06B.	FACT	Q2'26 release and 6-K
FY26 efficiency ratio near 20%; the US entry kept within about 100 bps of efficiency-ratio impact.	FACT (management guidance)	Q2'26 call, 13 Aug 2026
The $60M asks and $25M cap are the case's figures. $35M is about 15 bps of annualized revenue, about 1.1% of opex and about 0.2 points of efficiency ratio ($25M: about 0.15).	ASSUMPTION + CALCULATION	Case brief; Q2'26 figures
The MTeam dispute is about the growth-opex envelope (core vs new bets), not regulatory capital by entity.	ASSUMPTION	Case brief is silent
Spend above $25M only from H1 profit above plan, inside the efficiency-ratio guide in force, NPL 90+ on plan; CFO decides, Risk can block, IR sets disclosure.	RULE (proposed)	To agree with the CFO
Board in 4 weeks (assumed Tue 17 Nov); Investor Day 8 Dec 2026; the Board approves the capital plan before the Investor Day story is set.	FACT (dates) + ASSUMPTION	Case brief; Nu IR
HQ jurisdiction open. Nu is above the EUR 750M Pillar Two threshold; 2026 carve-out 9.4% of payroll, 7.4% of tangible assets.	FACT (rule) + ASSUMPTION (site)	OECD GloBE rules
Option scores and weights are our judgment; third-party benchmarks are context only.	ASSUMPTION	Slide 5; backup D
FY27 envelope: first release 1 Jan 2027, second at Q1 close (decided on Q1 data), 2H checkpoint (up to $25M) and reserve ($10M) at H1 close. Hub of 4-6 people.	ASSUMPTION	Calendar fiscal year; sizing is ours
The hub can run Nu-approved AI tools inside Nu's environment; Security and Risk approve data access before the agents go live.	ASSUMPTION	To confirm with Security and Risk
HQ jurisdiction open; two candidate sites go to term sheet; the site scorecard weights are our judgment (backup J).	ASSUMPTION	Case brief is silent

BACKUP B

Open an entity only when a license or tax substance requires it; officers and signing follow the stage

Stage	Trigger for a local entity	Setup	Officers, signing and insurance
1. Market test (new countries)	No local license needed and no taxable presence; served from an existing licensed entity or a partner bank (as the US is today, through Lead Bank, since 10 Sep 2026).	No local entity. Cross-border or partner model.	Central signing only. No local director. Prevents an accidental permanent establishment.
2. Licensed scale-up (US charter, new verticals)	A regulator requires a local licensed entity (deposits, lending, custody), or substance rules require local payroll and assets.	Dedicated licensed entity with its own capital plan and headroom.	Fit-and-proper directors; two central officers plus one local leader; dual signature above a set limit; D&O before activation.
3. Core hub (Mexico, a bank since Aug 2026; Colombia; the HQ)	Full banking or fintech license in force; local CFO in place (already so in Mexico and Colombia).	Full licensed entity; regional campus where the HQ lands.	Audit and Risk Committee oversight; dual signature above limits set by category; director liability insurance; annual review of powers of attorney. If the HQ sits inside an existing licensed entity: a powers-of-attorney update only.

Sources: Nu announcements (US launch via Lead Bank, 10 Sep 2026; OCC conditional approval, 29 Jan 2026; Mexico bank authorization, 10 Jul 2026; local finance leadership per the CFO appointment release). Signing limits are proposals.

BACKUP D

Every number is a sourced fact, a labeled assumption or context

Topic	Source and class	Data point	Where it is used
Nu scale and efficiency	Nu Q2'26 release and 6-K; Form 20-F | FACT	138.9M customers; ARPAC $17.1; cost to serve $1.0 ($0.8 a year earlier); efficiency ratio 19.5% (17.6% in Q1; ~20% FY26 per the call); ROE 33%; net income $1.06B; opex $806.2M; net revenue ~$4.1B; low-and-grow underwriting.	Slides 5, 7; backup A
Corporate events	Nu announcements; OCC; Nu IR | FACT	Mexico bank authorization 10 Jul 2026 (operating from 6 Aug), $4.2B plan to 2030; OCC conditional approval 29 Jan 2026 (capital within 12 months); US launch via Lead Bank 10 Sep 2026; buyback up to $1.0B (4 Jun 2026); CFO since 13 Jul 2026; Q3'26 results 12 Nov; Investor Day 8 Dec 2026.	Slides 9, 13; backup B
Cohorts	Q1'26 earnings presentation | FACT	$30.8 monthly ARPAC at 96 months since origination vs $15.9 total.	Slide 7 (70/30 split)
HQ tax rules	OECD GloBE Model Rules; Form 20-F | FACT (rule)	EUR 750M threshold; 15% minimum; 2026 transitional carve-out 9.4% of payroll and 7.4% of tangible assets (Art. 5.3, 9.2); Nu Holdings is Cayman-incorporated.	Slide 11
Context only	Hackett, McKinsey, Gartner, HBR, NACD, Deloitte, Baker McKenzie; three-horizons framing (Baghai, Coley and White) | CONTEXT	Central hubs shorten planning cycles; active reallocators earn higher returns; fair process wins acceptance; Board books at T-7.	Footers and talk only
AI in operations	Nu Q2'26 release; Nu newsroom (Hyperplane, Jun 2024) | FACT. Gartner; PMI; Science; HBS/BCG | CONTEXT	AI agents handle more than 60% of support chats in Brazil; AI-first strategy. Studies and surveys on AI in project reporting, writing and finance (backup H).	Slides 2, 3, 8, 14; backup H
Spend prioritization methodology	McKinsey, Deloitte	Studies support strategic initiative alignment, streamlined financial planning, compact schedules and regular in-year resource reallocation, with strategy-driven, granular allocation and clear senior decision rights.	Slide 6

Research assisted by AI tools, with every figure, calculation and recommendation checked personally.

BACKUP F

One timeline: tenure days, Board countdown and HQ gates

Tenure day	Date	Board countdown / HQ gate	What happens
Day 60	Tue 20 Oct	T-28 | HQ D+0	Board outline out; HQ charter signed; tax gate launched
Day 67	Tue 27 Oct	T-21	One-to-ones with each executive
Day 72	Early Nov	T-16	Capital options lock with CEO, CFO and MTeam
Day 78-81	Early Nov	T-10 to T-7	Inputs freeze; chairs briefed (T-9); book on portal (T-7)
Day 88	Tue 17 Nov (assumed)	T-0	Board approves FY27 plan; first-release allocation published
Day 90	Thu 19 Nov	HQ D+30	Gate 1: tax and residence opinion; two sites to term sheet
Day 95	Late Nov		Hub in place; market and vertical finance teams aligned
Day 105	Early Dec		Bi-weekly stand-ups running; business cases in review
Day 120	Mid-Dec	HQ D+60	Gate 2: grant terms (12-24 months' grace); one site dropped
Day 133	Fri 1 Jan 2027		FY27 starts; $15M first release
Day 150	Mid-Jan	HQ D+90	Gate 3: officers and D&O; 90-day report to the CFO
Day 180	Mid-Feb	HQ D+120	Gate 4: lease
Day 222	Wed 31 Mar		Q1 close; second release ($10M) decided on Q1 data in early April

BACKUP H

Proposed AI support across the four deliverables

Deliverable	PMO agent: coordination	Review agent: decision support
1 Planning & spend	Track case submissions, funding gates and monthly spend. Prepare status for quarterly GM reviews.	Check cases against the scorecard and source data. Flag assumption gaps and spend variances for Finance review.
2 C-suite & Board	Maintain the agenda and preparation tracker. Draft action updates for weekly CFO and monthly GM discussions.	Check papers against agreed decisions and source tables. Draft briefs and responses for executive sign-off before publication.
3 HQ project	Track workstreams, gate dependencies and decisions. Prepare weekly updates and monthly SteerCo packs.	Check gate packs for missing approvals, conflicting inputs and open risks. Route technical conclusions to the relevant SMEs.
4 Leadership & team	Track commitments across Country and BU teams. Compile overdue actions and review feedback.	Consolidate lessons and draft improvement options. Named owners validate analysis and recommendations.
Human control	Owners confirm status. People approve changes to dates and decisions. CoS & CG owns escalation to the CFO.	Use approved tools and source-linked inputs. Finance, executives and SMEs sign off. Agents never approve funding or commitments.

Pilot measures: reporting hours saved, on-time papers and gate packs, errors caught before sign-off, and overdue actions. Establish baselines before setting targets.

BACKUP J

HQ site scorecard and risk register: hard tests first, then weights

Hard tests first, pass or fail: license, tax residence and taxable presence, fit-and-proper officers, real payroll and assets. Only sites that pass are scored.

Criterion	Weight	Evidence and owner
Talent pool and wage cost	30	Hiring data and wage benchmarks (People)
Incentive value net of clawback	20	Draft terms with the clawback modeled (Legal, Tax)
Campus cost, flexibility and timing	20	Lease options, break clauses, fit-out time (Workplace)
Modeled tax rate under Pillar Two, including any domestic top-up	15	The gate 1 model (Tax)
Political and reputational risk	15	Local stakeholder map (Legal, Comms)

Risk	Mitigation	Owner
Tax residence or a taxable presence moves	Opinion at gate 1; meeting patterns unchanged; no early signing	Tax
Grant clawback	Proportional scaling and 12-24 months' grace; walk away from cliff-edge terms	Legal
Officer approval runs late	Files at gate 1; no activation before approval; the lease long-stop moves with it	Legal, People
Site politics and disclosure	No public contact before the scorecard; one spokesperson (Comms); IR decides what is disclosed and when	Comms, IR
Dependence on the CoS	A named deputy, the decision log, gate packs the CFO can decide on without the lead	CoS & CG

Weights and mitigations are our proposals. No savings figure until a site is chosen.

BACKUP K

How AI was used: an AI-supported case, not an AI-driven one

WHAT AI SUPPORTED

Research, checking and tidying

Research on Nu's public data, filings and announcements, and on planning and governance practices.

Numbers: calculations re-run and cross-checked against the sources.

References and best practices: sources found, read and summarized.

Minor formatting of slides and tables.

Testing some of the assumptions and scenarios (for example the option-weight sensitivity).

WHAT WAS HUMAN-BUILT

The thinking, the writing and the calls

The ideas, recommendations and judgments, and all the writing.

The structure, the storyline and the framing of each deliverable.

The assumptions, their classification as fact or assumption, and the trade-offs taken.

The final review of every figure, reference and recommendation.

The decision to present this as an AI-supported case rather than let AI drive it.

Tools: Claude, Gemini and Copilot were used, each for different aspects of the work; no single tool produced the case. **Looking ahead:** the AI agents proposed for the planning hub and the Board and HQ work (slide 3, backup H) can be set up in any LLM Nubank enables, inside Nu's environment and on approved tools, with people owning every number and decision.

Every figure, calculation, reference and recommendation in this deck was reviewed and is owned by the author.
